


Wloclawek Waste-to-Energy Project

CEO Executive Report - Procurement & Budget Snapshot

Report sintetico ad alta leggibilità, generato dai file Budget e Procurement



Curva S ordini vs pianificato

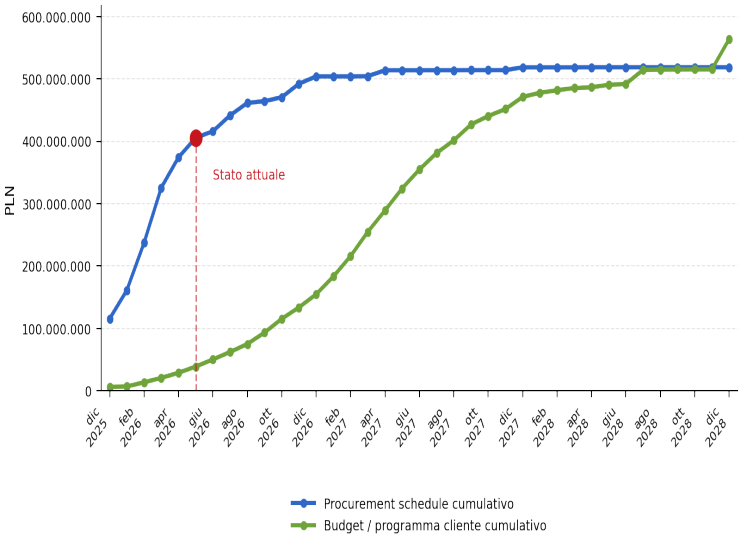

Mix ordini



Produzione annua dichiarata

Anno	Valore (PLN)
2025	6.199.140
2026	134.487.664
2027	300.887.569
2028	59.570.061

Milestones penalizzate

- 1 Water pressure test
- 2 Placement of the turbo-generator on the foundation
- 3 Measurement of guaranteed parameters A
- 4 Handover of the ITPO project to operation



Focus CEO - Messaggi chiave

- ✓ Il budget attuale è inferiore al Budget 0 di 3,9 mln PLN (-0,8%),
- ✓ 37,3% del valore procurement già ordinato; 40,7% ancora da ordinare.
- ✓ Nei prossimi 3 mesi sono previsti 61 ordini, con 40 ordini chiusi negli ultimi 3 mesi.
